

Lower room | boundary probing evidence

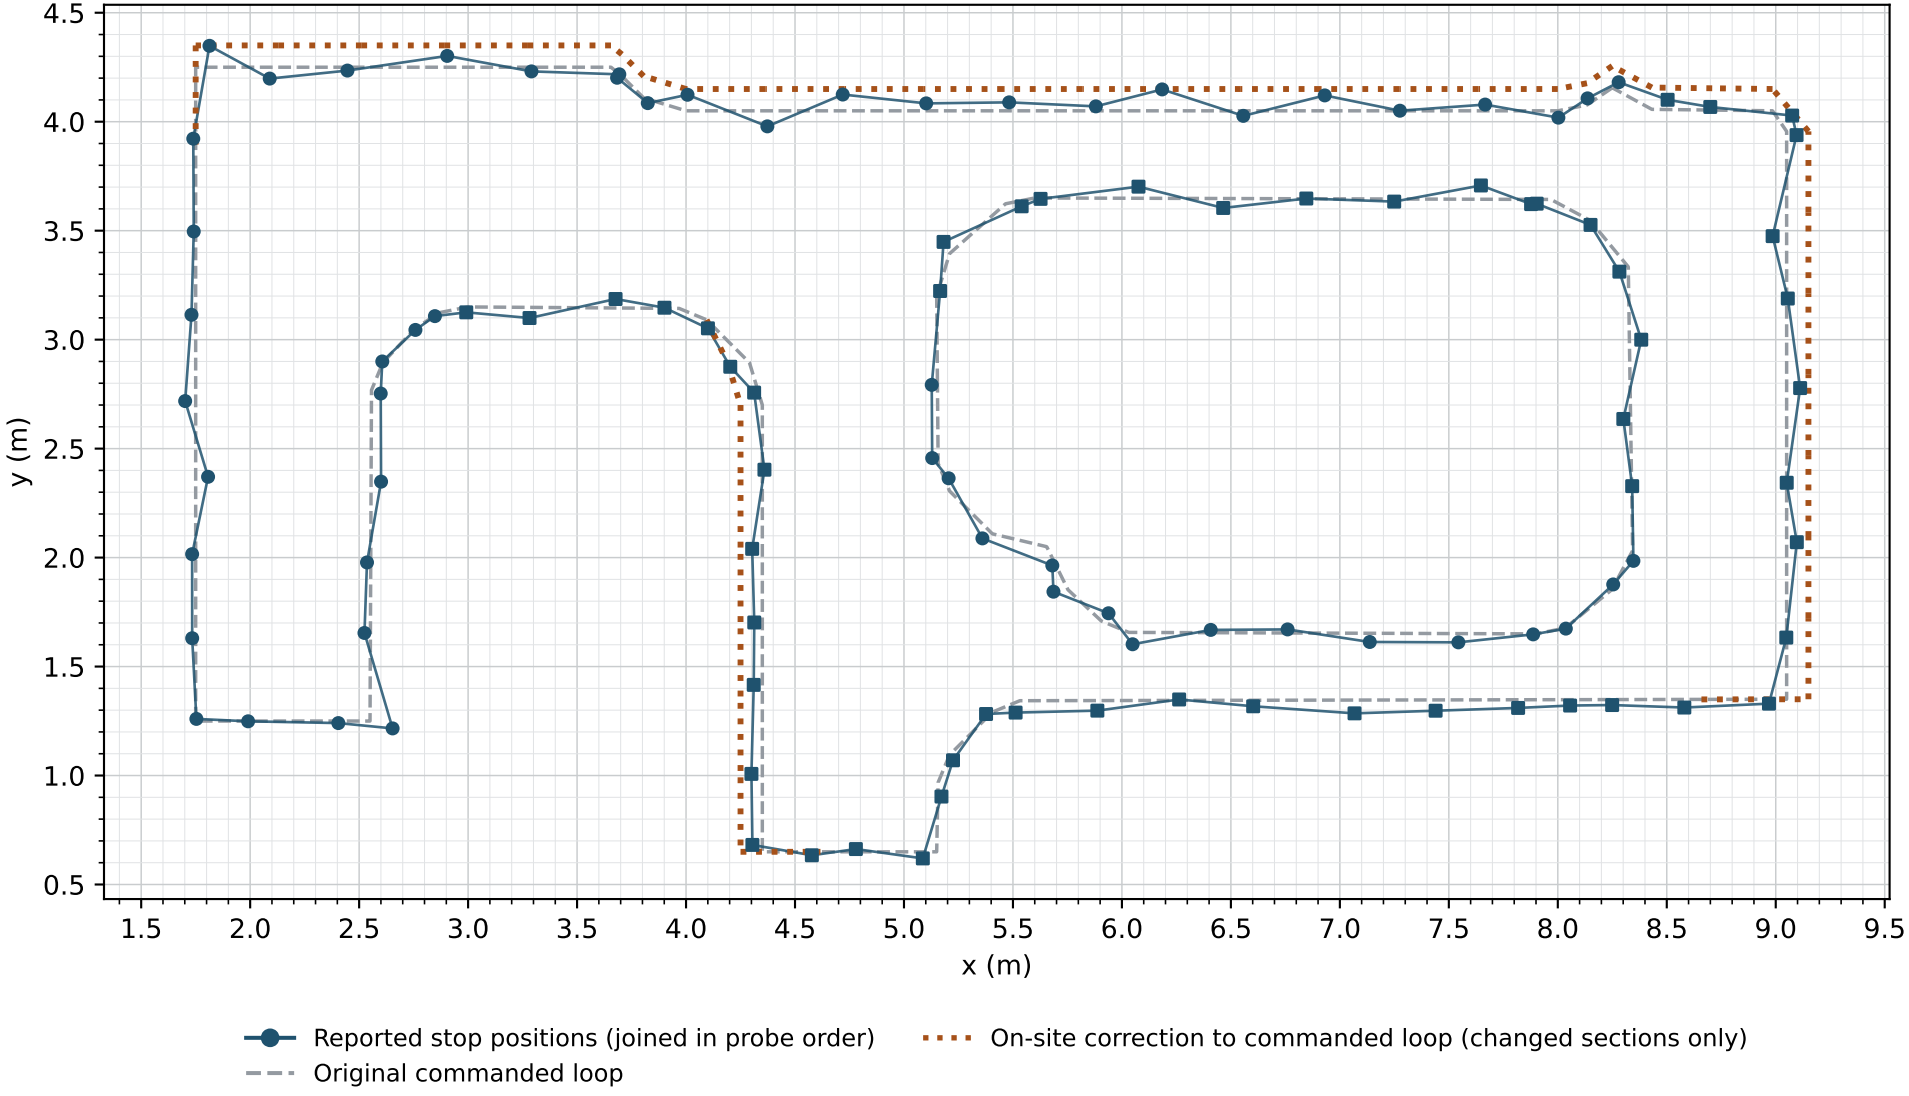

10 cm grid. Straight joins between reported stops are a sketch, not a continuous trajectory. No wall mask or buffer is used here.

Upper room | boundary probing evidence

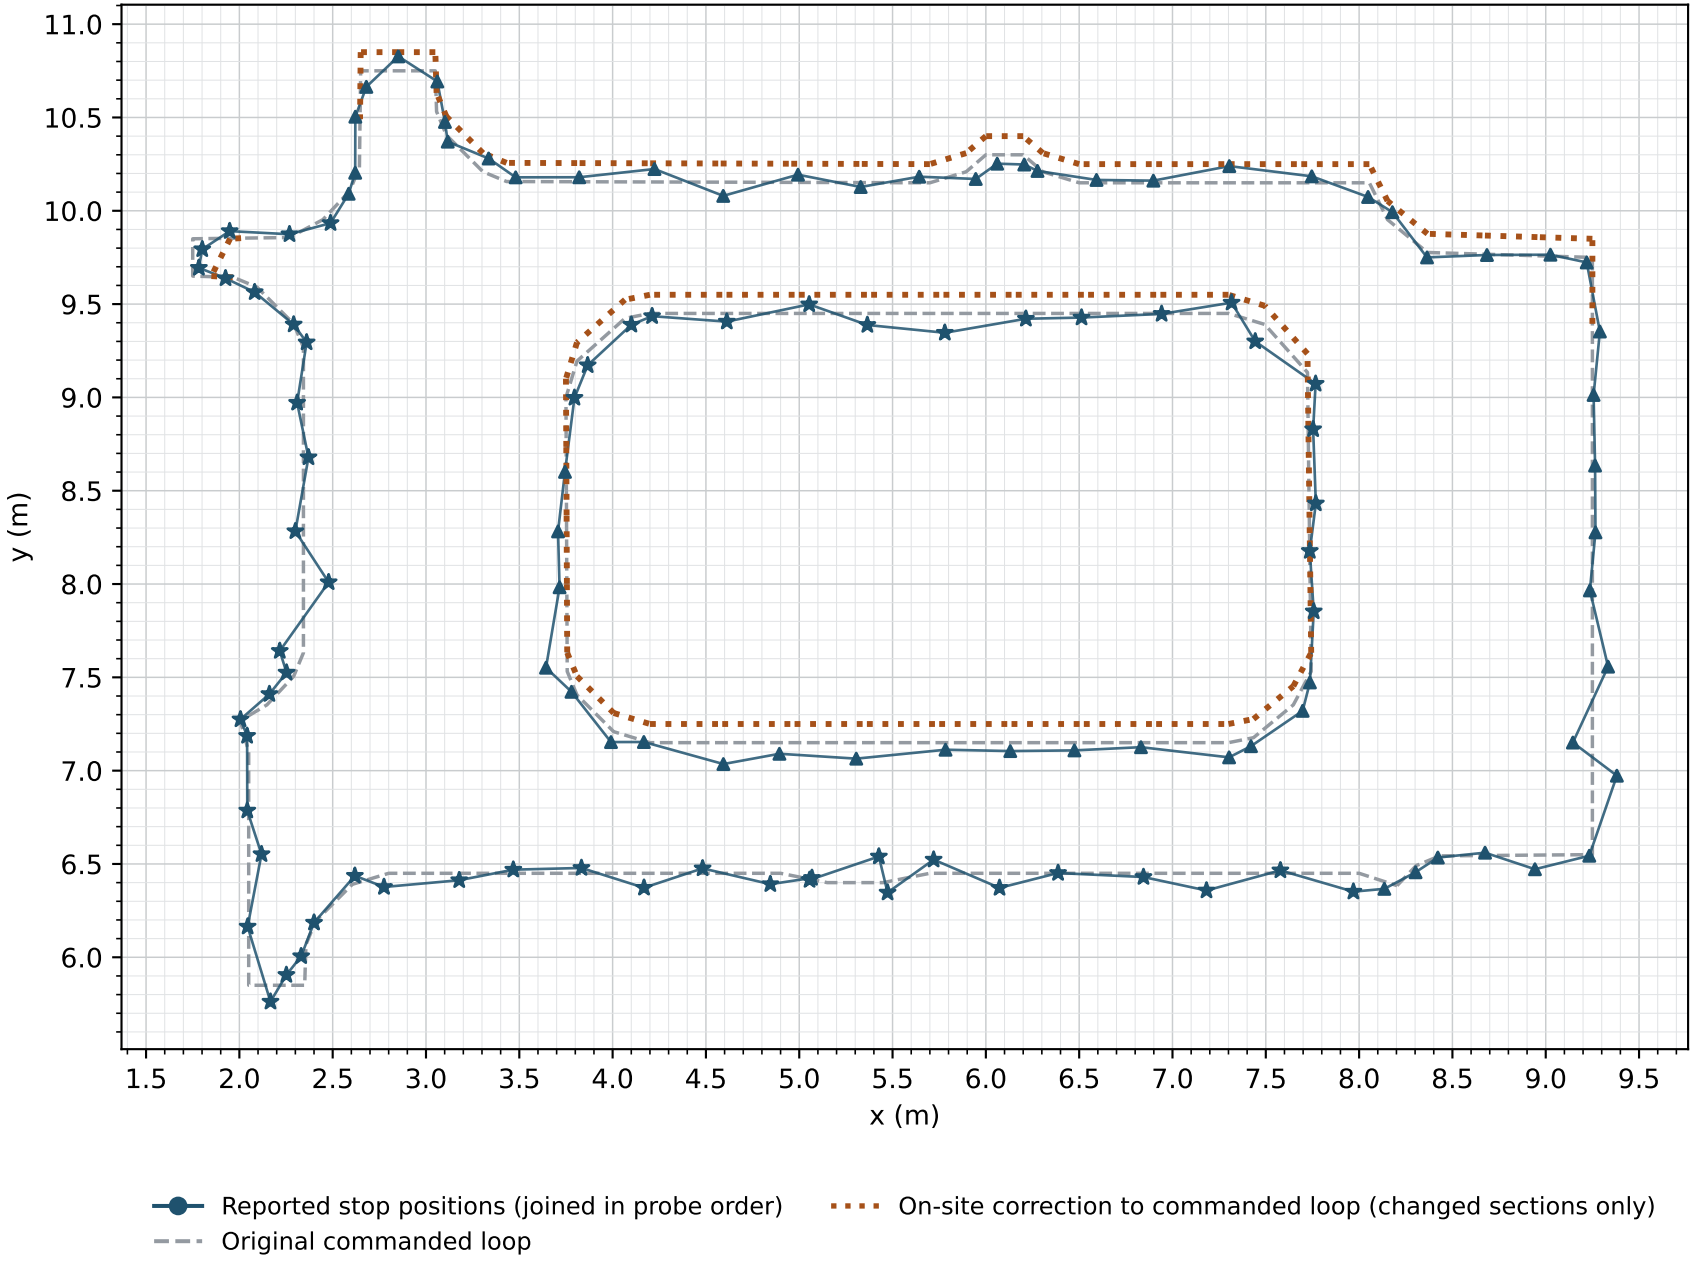

10 cm grid. Straight joins between reported stops are a sketch, not a continuous trajectory. No wall mask or buffer is used here.

Probe coordinates | row-level evidence

All positions in metres. Local dates: inner Nov 6; outer Nov 9. Row numbers include the CSV header.
Reported = median estimated position 60–<170 s after move issue, using fresh robot status (within 25 s of frame).
Approved = commanded point with on-site correction; it was not necessarily driven at that revised coordinate.

Probe	CSV row	Offset s	Command (x, y)	Reported (x, y)	Approved (x, y)	Frames
Inner	A#10	360	5.1534, 2.8159	5.1273, 2.7926	5.1534, 2.8159	11
Inner	A#14	540	5.1567, 2.4317	5.1294, 2.4566	5.1567, 2.4317	11
Inner	A#18	720	5.2090, 2.3056	5.2048, 2.3639	5.2090, 2.3056	11
Inner	A#22	900	5.4056, 2.1090	5.3599, 2.0881	5.4056, 2.1090	11
Inner	A#26	1080	5.6549, 2.0500	5.6806, 1.9637	5.6549, 2.0500	11
Inner	A#30	1260	5.7525, 1.8525	5.6858, 1.8435	5.7525, 1.8525	11
Inner	A#34	1440	5.9056, 1.7090	5.9384, 1.7445	5.9056, 1.7090	10
Inner	A#38	1620	6.0317, 1.6567	6.0490, 1.6023	6.0317, 1.6567	11
Inner	A#42	1800	6.4054, 1.6554	6.4076, 1.6682	6.4054, 1.6554	11
Inner	A#46	1980	6.7790, 1.6540	6.7602, 1.6704	6.7790, 1.6540	11
Inner	A#50	2160	7.1527, 1.6527	7.1372, 1.6128	7.1527, 1.6527	11
Inner	A#54	2340	7.5263, 1.6513	7.5438, 1.6111	7.5263, 1.6513	11
Inner	A#58	2520	7.9000, 1.6500	7.8870, 1.6476	7.9000, 1.6500	11
Inner	A#62	2700	8.0339, 1.6766	8.0368, 1.6741	8.0339, 1.6766	10
Inner	A#66	2880	8.2475, 1.8525	8.2542, 1.8768	8.2475, 1.8525	11
Inner	A#70	3060	8.3433, 2.0317	8.3469, 1.9850	8.3433, 2.0317	11
Inner	B#11	390	8.3383, 2.3573	8.3413, 2.3278	8.3383, 2.3573	11
Inner	B#15	570	8.3333, 2.6828	8.3007, 2.6361	8.3333, 2.6828	11
Inner	B#19	750	8.3283, 3.0084	8.3829, 2.9998	8.3283, 3.0084	11
Inner	B#23	930	8.3234, 3.3339	8.2826, 3.3120	8.3234, 3.3339	11
Inner	B#27	1110	8.1475, 3.5475	8.1502, 3.5265	8.1475, 3.5475	11
Inner	B#31	1290	7.9683, 3.6433	7.9032, 3.6239	7.9683, 3.6433	11
Inner	B#35	1470	7.7709, 3.6438	7.8774, 3.6219	7.7709, 3.6438	10
Inner	B#39	1650	7.5736, 3.6444	7.6472, 3.7075	7.5736, 3.6444	11
Inner	B#43	1830	7.1789, 3.6455	7.2493, 3.6334	7.1789, 3.6455	11
Inner	B#47	2010	6.7841, 3.6466	6.8461, 3.6476	6.7841, 3.6466	11
Inner	B#51	2190	6.3894, 3.6478	6.4647, 3.6042	6.3894, 3.6478	11
Inner	B#55	2370	5.9947, 3.6489	6.0760, 3.7020	5.9947, 3.6489	11
Inner	B#59	2550	5.6000, 3.6500	5.6267, 3.6460	5.6000, 3.6500	11
Inner	B#63	2730	5.4661, 3.6234	5.5399, 3.6118	5.4661, 3.6234	11
Inner	B#67	2910	5.2090, 3.3944	5.1817, 3.4485	5.2090, 3.3944	11
Inner	B#71	3090	5.1500, 3.2000	5.1658, 3.2232	5.1500, 3.2000	11
Inner	C#12	420	3.7517, 8.6329	3.7448, 8.6011	3.7517, 8.7329	11
Inner	C#16	600	3.7534, 8.2659	3.7075, 8.2820	3.7534, 8.3659	11
Inner	C#20	780	3.7550, 7.8988	3.7158, 7.9828	3.7550, 7.9988	10
Inner	C#24	960	3.7567, 7.5317	3.6429, 7.5517	3.7567, 7.6317	11

Probe coordinates | row-level evidence

All positions in metres. Local dates: inner Nov 6; outer Nov 9. Row numbers include the CSV header.
Reported = median estimated position 60–<170 s after move issue, using fresh robot status (within 25 s of frame).
Approved = commanded point with on-site correction; it was not necessarily driven at that revised coordinate.

Probe	CSV row	Offset s	Command (x, y)	Reported (x, y)	Approved (x, y)	Frames
Inner	C#28	1140	3.8090, 7.4056	3.7796, 7.4226	3.8090, 7.5056	11
Inner	C#32	1320	4.0056, 7.2090	3.9912, 7.1532	4.0056, 7.3090	11
Inner	C#36	1500	4.2000, 7.1500	4.1675, 7.1536	4.2000, 7.2500	10
Inner	C#40	1680	4.5875, 7.1500	4.5936, 7.0354	4.5875, 7.2500	11
Inner	C#44	1860	4.9750, 7.1500	4.8939, 7.0905	4.9750, 7.2500	11
Inner	C#48	2040	5.3625, 7.1500	5.3055, 7.0644	5.3625, 7.2500	10
Inner	C#52	2220	5.7500, 7.1500	5.7838, 7.1122	5.7500, 7.2500	11
Inner	C#56	2400	6.1375, 7.1500	6.1308, 7.1050	6.1375, 7.2500	11
Inner	C#60	2580	6.5250, 7.1500	6.4745, 7.1086	6.5250, 7.2500	11
Inner	C#64	2760	6.9125, 7.1500	6.8311, 7.1258	6.9125, 7.2500	11
Inner	C#68	2940	7.3000, 7.1500	7.3033, 7.0713	7.3000, 7.2500	11
Inner	C#72	3120	7.4339, 7.1766	7.4206, 7.1312	7.4339, 7.2766	11
Inner	C#74	3300	7.6475, 7.3525	7.6974, 7.3206	7.6475, 7.4525	10
Inner	C#76	3480	7.7433, 7.5317	7.7363, 7.4728	7.7433, 7.6317	11
Inner	D#13	450	7.7393, 7.8522	7.7568, 7.8534	7.7393, 7.9522	11
Inner	D#17	630	7.7353, 8.1726	7.7357, 8.1771	7.7353, 8.2726	11
Inner	D#21	810	7.7313, 8.4931	7.7681, 8.4318	7.7313, 8.5931	10
Inner	D#25	990	7.7273, 8.8135	7.7536, 8.8293	7.7273, 8.9135	11
Inner	D#29	1170	7.7234, 9.1339	7.7670, 9.0730	7.7234, 9.2339	11
Inner	D#33	1350	7.4944, 9.3910	7.4433, 9.3002	7.4944, 9.4910	11
Inner	D#37	1530	7.3000, 9.4500	7.3166, 9.5077	7.3000, 9.5500	11
Inner	D#41	1710	6.9125, 9.4500	6.9418, 9.4474	6.9125, 9.5500	11
Inner	D#45	1890	6.5250, 9.4500	6.5127, 9.4278	6.5250, 9.5500	11
Inner	D#49	2070	6.1375, 9.4500	6.2145, 9.4214	6.1375, 9.5500	10
Inner	D#53	2250	5.7500, 9.4500	5.7801, 9.3464	5.7500, 9.5500	11
Inner	D#57	2430	5.3625, 9.4500	5.3649, 9.3881	5.3625, 9.5500	11
Inner	D#61	2610	4.9750, 9.4500	5.0532, 9.4986	4.9750, 9.5500	10
Inner	D#65	2790	4.5875, 9.4500	4.6119, 9.4061	4.5875, 9.5500	11
Inner	D#69	2970	4.2000, 9.4500	4.2115, 9.4352	4.2000, 9.5500	11
Inner	D#73	3150	4.0661, 9.4234	4.1005, 9.3894	4.0661, 9.5234	11
Inner	D#75	3330	3.8090, 9.1944	3.8665, 9.1721	3.8090, 9.2944	10
Inner	D#77	3510	3.7500, 9.0000	3.7955, 8.9979	3.7500, 9.1000	11
Outer	A#10	360	8.2500, 4.1556	8.2792, 4.1812	8.2500, 4.2556	11
Outer	A#14	540	8.1339, 4.0766	8.1366, 4.1071	8.1339, 4.1766	10
Outer	A#18	720	8.0000, 4.0500	8.0027, 4.0187	8.0000, 4.1500	11
Outer	A#22	900	7.6364, 4.0500	7.6666, 4.0786	7.6364, 4.1500	11

Probe coordinates | row-level evidence

All positions in metres. Local dates: inner Nov 6; outer Nov 9. Row numbers include the CSV header.
Reported = median estimated position 60–<170 s after move issue, using fresh robot status (within 25 s of frame).
Approved = commanded point with on-site correction; it was not necessarily driven at that revised coordinate.

Probe	CSV row	Offset s	Command (x, y)	Reported (x, y)	Approved (x, y)	Frames
Outer	A#26	1080	7.2727, 4.0500	7.2754, 4.0505	7.2727, 4.1500	10
Outer	A#30	1260	6.9091, 4.0500	6.9307, 4.1207	6.9091, 4.1500	11
Outer	A#34	1440	6.5455, 4.0500	6.5569, 4.0268	6.5455, 4.1500	11
Outer	A#38	1620	6.1818, 4.0500	6.1844, 4.1482	6.1818, 4.1500	11
Outer	A#42	1800	5.8182, 4.0500	5.8804, 4.0704	5.8182, 4.1500	10
Outer	A#46	1980	5.4545, 4.0500	5.4827, 4.0888	5.4545, 4.1500	11
Outer	A#50	2160	5.0909, 4.0500	5.1019, 4.0841	5.0909, 4.1500	11
Outer	A#54	2340	4.7273, 4.0500	4.7190, 4.1247	4.7273, 4.1500	11
Outer	A#58	2520	4.3636, 4.0500	4.3731, 3.9787	4.3636, 4.1500	11
Outer	A#62	2700	4.0000, 4.0500	4.0067, 4.1237	4.0000, 4.1500	11
Outer	A#66	2880	3.8056, 4.1090	3.8244, 4.0853	3.8056, 4.2090	10
Outer	A#70	3060	3.7056, 4.2090	3.6837, 4.2017	3.7056, 4.3090	11
Outer	A#74	3240	3.6556, 4.2500	3.6938, 4.2174	3.6556, 4.3500	11
Outer	A#78	3420	3.2745, 4.2500	3.2907, 4.2308	3.2745, 4.3500	10
Outer	A#82	3600	2.8933, 4.2500	2.9041, 4.3019	2.8933, 4.3500	11
Outer	A#86	3780	2.5122, 4.2500	2.4463, 4.2346	2.5122, 4.3500	11
Outer	A#90	3960	2.1311, 4.2500	2.0898, 4.1978	2.1311, 4.3500	11
Outer	A#94	4140	1.7500, 4.2500	1.8134, 4.3482	1.7500, 4.3500	11
Outer	A#98	4320	1.7500, 3.8750	1.7390, 3.9221	1.7500, 3.8750	11
Outer	A#102	4500	1.7500, 3.5000	1.7411, 3.4963	1.7500, 3.5000	11
Outer	A#106	4680	1.7500, 3.1250	1.7308, 3.1140	1.7500, 3.1250	11
Outer	A#110	4860	1.7500, 2.7500	1.7018, 2.7182	1.7500, 2.7500	11
Outer	A#114	5040	1.7500, 2.3750	1.8069, 2.3707	1.7500, 2.3750	11
Outer	A#118	5220	1.7500, 2.0000	1.7338, 2.0158	1.7500, 2.0000	10
Outer	A#122	5400	1.7500, 1.6250	1.7340, 1.6300	1.7500, 1.6250	11
Outer	A#126	5580	1.7500, 1.2500	1.7532, 1.2598	1.7500, 1.2500	11
Outer	A#130	5760	2.0167, 1.2500	1.9907, 1.2488	2.0167, 1.2500	10
Outer	A#134	5940	2.2833, 1.2500	2.4047, 1.2406	2.2833, 1.2500	11
Outer	A#138	6120	2.5500, 1.2500	2.6536, 1.2162	2.5500, 1.2500	11
Outer	A#142	6300	2.5517, 1.6296	2.5245, 1.6542	2.5517, 1.6296	11
Outer	A#146	6480	2.5534, 2.0091	2.5361, 1.9777	2.5534, 2.0091	11
Outer	A#150	6660	2.5550, 2.3887	2.6007, 2.3484	2.5550, 2.3887	11
Outer	A#154	6840	2.5567, 2.7683	2.5991, 2.7528	2.5567, 2.7683	11
Outer	A#158	7020	2.6090, 2.8944	2.6062, 2.8999	2.6090, 2.8944	11
Outer	A#162	7200	2.7525, 3.0475	2.7583, 3.0446	2.7525, 3.0475	11
Outer	A#166	7380	2.8661, 3.1234	2.8477, 3.1079	2.8661, 3.1234	11

Probe coordinates | row-level evidence

All positions in metres. Local dates: inner Nov 6; outer Nov 9. Row numbers include the CSV header.
Reported = median estimated position 60–<170 s after move issue, using fresh robot status (within 25 s of frame).
Approved = commanded point with on-site correction; it was not necessarily driven at that revised coordinate.

Probe	CSV row	Offset s	Command (x, y)	Reported (x, y)	Approved (x, y)	Frames
Outer	B#11	390	3.0000, 3.1500	2.9916, 3.1253	3.0000, 3.1500	11
Outer	B#15	570	3.3228, 3.1478	3.2819, 3.0993	3.3228, 3.1478	10
Outer	B#19	750	3.6455, 3.1455	3.6766, 3.1865	3.6455, 3.1455	11
Outer	B#23	930	3.9683, 3.1433	3.9010, 3.1465	3.9683, 3.1433	11
Outer	B#27	1110	4.0944, 3.0910	4.1004, 3.0519	4.0944, 3.0910	10
Outer	B#31	1290	4.2910, 2.8944	4.2029, 2.8756	4.1910, 2.8944	11
Outer	B#35	1470	4.3500, 2.7000	4.3124, 2.7570	4.2500, 2.7000	11
Outer	B#39	1650	4.3500, 2.3583	4.3598, 2.4033	4.2500, 2.3583	10
Outer	B#43	1830	4.3500, 2.0167	4.3035, 2.0400	4.2500, 2.0167	11
Outer	B#47	2010	4.3500, 1.6750	4.3131, 1.7022	4.2500, 1.6750	11
Outer	B#51	2190	4.3500, 1.3333	4.3106, 1.4159	4.2500, 1.3333	11
Outer	B#55	2370	4.3500, 0.9917	4.3001, 1.0075	4.2500, 0.9917	11
Outer	B#59	2550	4.3500, 0.6500	4.3045, 0.6816	4.2500, 0.6500	11
Outer	B#63	2730	4.6167, 0.6500	4.5773, 0.6341	4.6167, 0.6500	11
Outer	B#67	2910	4.8833, 0.6500	4.7793, 0.6626	4.8833, 0.6500	11
Outer	B#71	3090	5.1500, 0.6500	5.0864, 0.6197	5.1500, 0.6500	11
Outer	B#75	3270	5.1567, 0.9683	5.1719, 0.9035	5.1567, 0.9683	11
Outer	B#79	3450	5.2090, 1.0944	5.2249, 1.0699	5.2090, 1.0944	10
Outer	B#83	3630	5.4056, 1.2910	5.3766, 1.2822	5.4056, 1.2910	11
Outer	B#87	3810	5.5317, 1.3433	5.5122, 1.2888	5.5317, 1.3433	11
Outer	B#91	3990	5.9226, 1.3440	5.8873, 1.2978	5.9226, 1.3440	10
Outer	B#95	4170	6.3136, 1.3448	6.2626, 1.3490	6.3136, 1.3448	11
Outer	B#99	4350	6.7045, 1.3455	6.6022, 1.3177	6.7045, 1.3455	11
Outer	B#103	4530	7.0954, 1.3463	7.0673, 1.2853	7.0954, 1.3463	11
Outer	B#107	4710	7.4863, 1.3470	7.4393, 1.2973	7.4863, 1.3470	11
Outer	B#111	4890	7.8772, 1.3478	7.8179, 1.3102	7.8772, 1.3478	11
Outer	B#115	5070	8.0727, 1.3481	8.0565, 1.3211	8.0727, 1.3481	11
Outer	B#119	5250	8.2682, 1.3485	8.2493, 1.3234	8.2682, 1.3485	11
Outer	B#123	5430	8.6591, 1.3493	8.5805, 1.3119	8.6591, 1.3493	11
Outer	B#127	5610	9.0500, 1.3500	8.9689, 1.3298	9.1500, 1.3500	11
Outer	B#131	5790	9.0500, 1.7222	9.0484, 1.6329	9.1500, 1.7222	10
Outer	B#135	5970	9.0500, 2.0944	9.0968, 2.0706	9.1500, 2.0944	11
Outer	B#139	6150	9.0500, 2.4667	9.0504, 2.3434	9.1500, 2.4667	11
Outer	B#143	6330	9.0500, 2.8389	9.1120, 2.7778	9.1500, 2.8389	10
Outer	B#147	6510	9.0500, 3.2111	9.0553, 3.1887	9.1500, 3.2111	11
Outer	B#151	6690	9.0500, 3.5833	8.9857, 3.4750	9.1500, 3.5833	11

Probe coordinates | row-level evidence

All positions in metres. Local dates: inner Nov 6; outer Nov 9. Row numbers include the CSV header.
Reported = median estimated position 60–<170 s after move issue, using fresh robot status (within 25 s of frame).
Approved = commanded point with on-site correction; it was not necessarily driven at that revised coordinate.

Probe	CSV row	Offset s	Command (x, y)	Reported (x, y)	Approved (x, y)	Frames
Outer	B#155	6870	9.0500, 3.9556	9.0956, 3.9385	9.1500, 3.9556	11
Outer	B#159	7050	8.9852, 4.0500	9.0754, 4.0282	8.9852, 4.1500	11
Outer	B#163	7230	8.7085, 4.0534	8.6997, 4.0677	8.7085, 4.1534	11
Outer	B#167	7410	8.4317, 4.0567	8.5038, 4.1006	8.4317, 4.1567	11
Outer	C#12	420	8.2033, 6.3838	8.1352, 6.3668	8.2033, 6.3838	11
Outer	C#16	600	8.3056, 6.4910	8.3024, 6.4556	8.3056, 6.4910	11
Outer	C#20	780	8.4317, 6.5433	8.4220, 6.5344	8.4317, 6.5433	11
Outer	C#24	960	8.7045, 6.5455	8.6747, 6.5604	8.7045, 6.5455	11
Outer	C#28	1140	8.9772, 6.5478	8.9422, 6.4718	8.9772, 6.5478	10
Outer	C#32	1320	9.2500, 6.5500	9.2334, 6.5441	9.2500, 6.5500	11
Outer	C#36	1500	9.2500, 6.9056	9.3812, 6.9730	9.2500, 6.9056	11
Outer	C#40	1680	9.2500, 7.2611	9.1455, 7.1507	9.2500, 7.2611	10
Outer	C#44	1860	9.2500, 7.6167	9.3341, 7.5574	9.2500, 7.6167	11
Outer	C#48	2040	9.2500, 7.9722	9.2366, 7.9659	9.2500, 7.9722	11
Outer	C#52	2220	9.2500, 8.3278	9.2665, 8.2770	9.2500, 8.3278	11
Outer	C#56	2400	9.2500, 8.6833	9.2644, 8.6350	9.2500, 8.6833	11
Outer	C#60	2580	9.2500, 9.0389	9.2565, 9.0132	9.2500, 9.0389	11
Outer	C#64	2760	9.2500, 9.3944	9.2902, 9.3532	9.2500, 9.3944	11
Outer	C#68	2940	9.2500, 9.7500	9.2196, 9.7233	9.2500, 9.8500	11
Outer	C#72	3120	8.9554, 9.7589	9.0251, 9.7646	8.9554, 9.8589	11
Outer	C#76	3300	8.6607, 9.7678	8.6850, 9.7631	8.6607, 9.8678	11
Outer	C#80	3480	8.3661, 9.7766	8.3639, 9.7502	8.3661, 9.8766	10
Outer	C#84	3660	8.1525, 9.9525	8.1785, 9.9927	8.1525, 10.0525	11
Outer	C#88	3840	8.0549, 10.1500	8.0481, 10.0741	8.0549, 10.2500	11
Outer	C#92	4020	7.6662, 10.1500	7.7464, 10.1847	7.6662, 10.2500	10
Outer	C#96	4200	7.2775, 10.1500	7.3045, 10.2394	7.2775, 10.2500	11
Outer	C#100	4380	6.8887, 10.1500	6.8975, 10.1615	6.8887, 10.2500	11
Outer	C#104	4560	6.5000, 10.1500	6.5929, 10.1653	6.5000, 10.2500	10
Outer	C#108	4740	6.3056, 10.2090	6.2767, 10.2136	6.3056, 10.3090	11
Outer	C#112	4920	6.2000, 10.3000	6.2058, 10.2479	6.2000, 10.4000	11
Outer	C#116	5100	6.0000, 10.3000	6.0607, 10.2525	6.0000, 10.4000	11
Outer	C#120	5280	5.8944, 10.2090	5.9459, 10.1705	5.8944, 10.3090	11
Outer	C#124	5460	5.7000, 10.1500	5.6428, 10.1826	5.7000, 10.2500	11
Outer	C#128	5640	5.3220, 10.1511	5.3292, 10.1275	5.3220, 10.2511	11
Outer	C#132	5820	4.9439, 10.1522	4.9933, 10.1935	4.9439, 10.2522	10
Outer	C#136	6000	4.5659, 10.1534	4.5927, 10.0799	4.5659, 10.2534	11

Probe coordinates | row-level evidence

All positions in metres. Local dates: inner Nov 6; outer Nov 9. Row numbers include the CSV header.
Reported = median estimated position 60–<170 s after move issue, using fresh robot status (within 25 s of frame).
Approved = commanded point with on-site correction; it was not necessarily driven at that revised coordinate.

Probe	CSV row	Offset s	Command (x, y)	Reported (x, y)	Approved (x, y)	Frames
Outer	C#140	6180	4.1878, 10.1545	4.2243, 10.2238	4.1878, 10.2545	11
Outer	C#144	6360	3.8098, 10.1556	3.8210, 10.1797	3.8098, 10.2556	10
Outer	C#148	6540	3.4317, 10.1567	3.4805, 10.1792	3.4317, 10.2567	11
Outer	C#152	6720	3.3056, 10.2090	3.3358, 10.2802	3.3056, 10.3090	11
Outer	C#156	6900	3.1090, 10.4056	3.1165, 10.3706	3.1090, 10.5056	10
Outer	C#160	7080	3.0567, 10.5317	3.1016, 10.4761	3.0567, 10.6317	11
Outer	C#164	7260	3.0500, 10.7500	3.0608, 10.6929	3.0500, 10.8500	11
Outer	C#168	7440	2.8500, 10.7500	2.8516, 10.8273	2.8500, 10.8500	11
Outer	C#170	7620	2.6500, 10.7500	2.6804, 10.6641	2.6500, 10.8500	11
Outer	C#172	7800	2.6466, 10.4909	2.6214, 10.5041	2.6466, 10.4909	11
Outer	C#174	7980	2.6433, 10.2317	2.6206, 10.2038	2.6433, 10.2317	11
Outer	C#176	8160	2.5910, 10.1056	2.5857, 10.0913	2.5910, 10.1056	11
Outer	D#13	450	2.4475, 9.9525	2.4885, 9.9339	2.4475, 9.9525	11
Outer	D#17	630	2.2683, 9.8567	2.2686, 9.8743	2.2683, 9.8567	11
Outer	D#21	810	2.0091, 9.8534	1.9481, 9.8910	2.0091, 9.8534	11
Outer	D#25	990	1.7500, 9.8500	1.8010, 9.7938	1.9500, 9.8500	11
Outer	D#29	1170	1.7500, 9.6500	1.7830, 9.6943	1.8500, 9.6500	11
Outer	D#33	1350	1.9683, 9.6433	1.9259, 9.6382	1.9683, 9.6433	11
Outer	D#37	1530	2.0944, 9.5910	2.0821, 9.5638	2.0944, 9.5910	11
Outer	D#41	1710	2.2910, 9.3944	2.2909, 9.3907	2.2910, 9.3944	10
Outer	D#45	1890	2.3433, 9.2683	2.3604, 9.2949	2.3433, 9.2683	11
Outer	D#49	2070	2.3433, 8.9410	2.3094, 8.9714	2.3433, 8.9410	11
Outer	D#53	2250	2.3433, 8.6137	2.3702, 8.6789	2.3433, 8.6137	10
Outer	D#57	2430	2.3433, 8.2863	2.3000, 8.2828	2.3433, 8.2863	11
Outer	D#61	2610	2.3433, 7.9590	2.4784, 8.0095	2.3433, 7.9590	11
Outer	D#65	2790	2.3433, 7.6317	2.2165, 7.6414	2.3433, 7.6317	11
Outer	D#69	2970	2.2910, 7.5056	2.2528, 7.5255	2.2910, 7.5056	11
Outer	D#73	3150	2.1475, 7.3525	2.1609, 7.4103	2.1475, 7.3525	11
Outer	D#77	3330	2.0052, 7.2679	2.0060, 7.2747	2.0052, 7.2679	11
Outer	D#81	3510	2.0500, 7.1000	2.0415, 7.1863	2.0500, 7.1000	11
Outer	D#85	3690	2.0500, 6.7875	2.0423, 6.7862	2.0500, 6.7875	11
Outer	D#89	3870	2.0500, 6.4750	2.1186, 6.5523	2.0500, 6.4750	11
Outer	D#93	4050	2.0500, 6.1625	2.0443, 6.1643	2.0500, 6.1625	10
Outer	D#97	4230	2.0500, 5.8500	2.1667, 5.7621	2.0500, 5.8500	11
Outer	D#101	4410	2.3500, 5.8500	2.2518, 5.9053	2.3500, 5.8500	11
Outer	D#105	4590	2.3567, 6.0683	2.3310, 6.0055	2.3567, 6.0683	10

Probe coordinates | row-level evidence

All positions in metres. Local dates: inner Nov 6; outer Nov 9. Row numbers include the CSV header.
Reported = median estimated position 60–<170 s after move issue, using fresh robot status (within 25 s of frame).
Approved = commanded point with on-site correction; it was not necessarily driven at that revised coordinate.

Probe	CSV row	Offset s	Command (x, y)	Reported (x, y)	Approved (x, y)	Frames
Outer	D#109	4770	2.4090, 6.1944	2.4000, 6.1855	2.4090, 6.1944	11
Outer	D#113	4950	2.6056, 6.3910	2.6189, 6.4367	2.6056, 6.3910	11
Outer	D#117	5130	2.8000, 6.4500	2.7750, 6.3766	2.8000, 6.4500	10
Outer	D#121	5310	3.1500, 6.4500	3.1780, 6.4128	3.1500, 6.4500	11
Outer	D#125	5490	3.5000, 6.4500	3.4679, 6.4695	3.5000, 6.4500	11
Outer	D#129	5670	3.8500, 6.4500	3.8330, 6.4785	3.8500, 6.4500	11
Outer	D#133	5850	4.2000, 6.4500	4.1682, 6.3725	4.2000, 6.4500	11
Outer	D#137	6030	4.5500, 6.4500	4.4822, 6.4764	4.5500, 6.4500	11
Outer	D#141	6210	4.9000, 6.4500	4.8450, 6.3916	4.9000, 6.4500	11
Outer	D#145	6390	5.0339, 6.4234	5.0681, 6.4252	5.0339, 6.4234	10
Outer	D#149	6570	5.1500, 6.4000	5.0552, 6.4144	5.1500, 6.4000	11
Outer	D#153	6750	5.4500, 6.4000	5.4266, 6.5399	5.4500, 6.4000	11
Outer	D#157	6930	5.5661, 6.4234	5.4733, 6.3467	5.5661, 6.4234	10
Outer	D#161	7110	5.7000, 6.4500	5.7201, 6.5233	5.7000, 6.4500	11
Outer	D#165	7290	6.0833, 6.4500	6.0732, 6.3718	6.0833, 6.4500	11
Outer	D#169	7470	6.4667, 6.4500	6.3869, 6.4516	6.4667, 6.4500	10
Outer	D#171	7650	6.8500, 6.4500	6.8445, 6.4300	6.8500, 6.4500	11
Outer	D#173	7830	7.2333, 6.4500	7.1822, 6.3579	7.2333, 6.4500	11
Outer	D#175	8010	7.6167, 6.4500	7.5782, 6.4657	7.6167, 6.4500	11
Outer	D#177	8190	8.0000, 6.4500	7.9694, 6.3517	8.0000, 6.4500	11
